

Lift 05

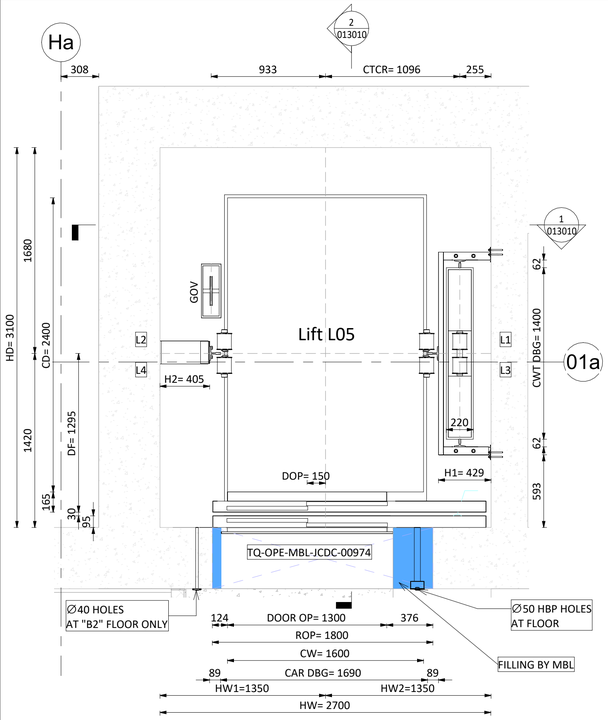


1 Hoist Way Plan At "B2" Floor - ELEV-L5

1 : 25

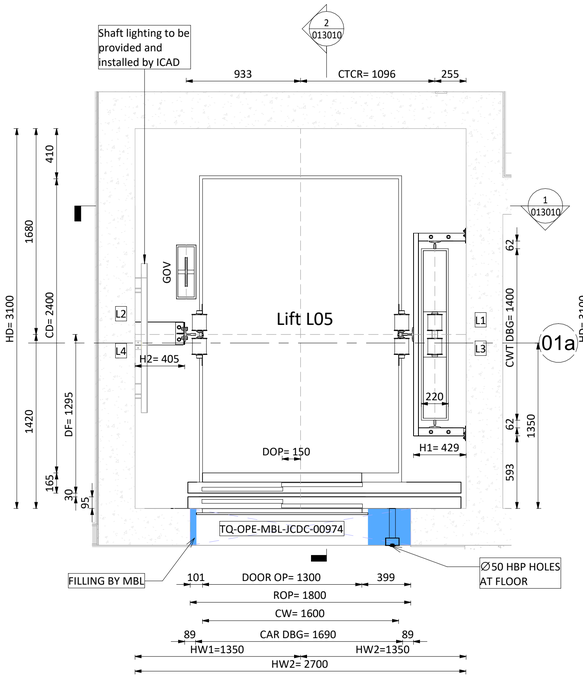


2 Hoist Way Plan At "G" Floor - ELEV-L5

1 : 25

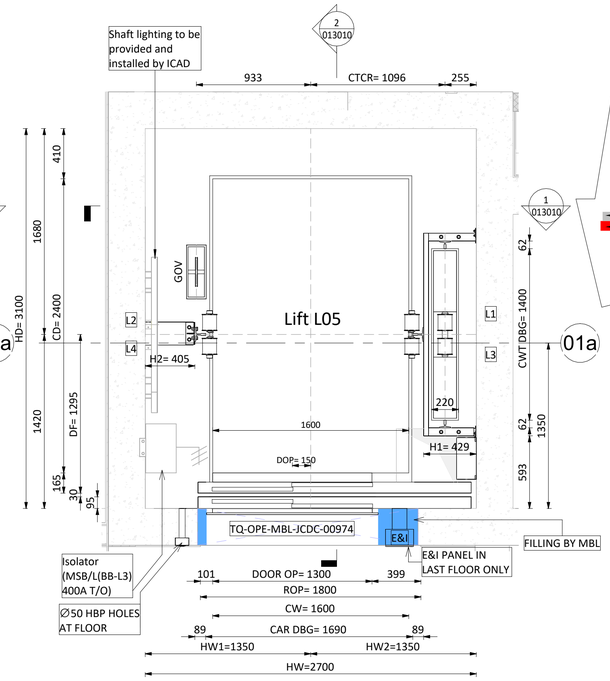


3 Hoist Way Plan At "Top" Floor - ELEV-L5

1 : 25

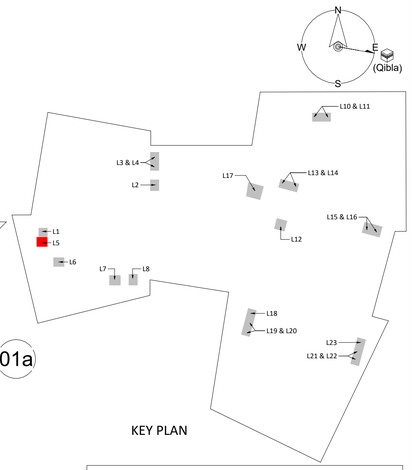

KEY PLAN




KEY PLAN

GENERAL NOTES: ALL LEVELS SHOWN ON THE DRAWING ARE CHART DATUM LEVELS PROJECT LEVEL+0.000 = +3.700 CHART DATUM.

ELEV-L5 ELEVATOR GENERAL SPECIFICATIONS	
LIFT NUMBER	ELEV.L5
CABIN INTERNAL SIZE(WXDXH)	1600X2400X2600
CAPACITY	2000 Kg
CLEAR ENTRANCE	1300X2400
CONTROL	VVVF
CONTROL SYSTEM	SIMPLEX FULL COLLECTIVE
COUNTERWEIGHT SAFETY	NO
DOOR TYPE	TLD2
EMERGENCY EXITS	-
FRONT OPENING	3
HEAT RELEASE	1774Kcal/h
HOISTWAY SIZE(HWXHD)	2700X3100
LIFT NUMBER	ELV.L5
LIGHTING SUPPLY	220V 60HZ
MIN.FLOOR HEIGHT	-
NO. OF FLOOR	4
NO. OF OPENINGS	3
NO. OF UNITS	1
NON-STOP FLOORS	1
NON-STOP FLOORS NAMES	B1
NUMBER OF PASSENGERS	26P
OVERHEAD	4500mm
PIT DEPTH	1600mm
POWER SUPPLY	380V 3P 60HZ
PRODUCT NO.	GeN2 MRL
RATED CURRENT(A)	31.4
REAR OPENING	-
ROPING	2:1
SPEED(m/s)	1.00
START CURRENT(A)	34.4
SYSTEM POWER(KW)	16.6
TRAVEL	13825mm
USE	WASTE LIFT

REACTIONS FORCE (KN)

Car side rail	CWT guide rail	Pit reaction
R= 91	R= 26	U= 188
R1= 4.24	R1= 1.76	V= 147
R2= 2.95	R2= 0.28	



LEGEND	
HW	HOIST WAY WIDTH
HD	HOIST WAY DEPTH
CRH	CAR ROUGH HEIGHT
DOOR OP	DOOR OPENING
ROP	ROUGH OPENING
CW	CAR WIDTH
CD	CAR DEPTH
CH	CAR HEIGHT
DBG	DISTANCE BETWEEN GUARDRAIL
CWT	COUNTERWEIGHT
E&I PANEL	EMERGENCY & INSPECTION PANEL
G.O.V	CAR GOVERNOR
COP	CAR OPERATING PANEL
HBP	HALL POSITION INDICATOR
	CONCRETE
	BLOCK

NOTE No.:
FRONT WALLS,FINISHES & ARCHITRAVES
TO BE BUILT (BY CLIENT) AFTER THE INSTALLATION OF
THE (LANDING) EXTERNAL DOORS.

IMPORTANT NOTE FOR MAIN CONTRACTOR.
FREEDOM OF ACCESS MUST BE AVAILABLE FOR POINT OF ENTRY INTO THE BUILDING UP TO THE ELEVATOR HOIST WAY AND THE FRONT WALLS OF THE HOIST WAY AT MAIN FLOOR TO BE LEFT OPEN FOR FULL WIDTH AND HEIGHT TO PERMIT ENTRY OF OUR EQUIPMENT.

DRAWING / DOCUMENT REFERENCE

NO.	NUMBER	TITLE	REV.
01	L-05	JOH-HLA-S4-01-056-XXX-01-DR-AR-011110	F00
02		JOH-BHC-S4-01-056-XXX-XX-DR-VT-015001	
03		JOH-BHC-S4-01-056-XXX-XX-DR-VT-010001	
04		JOH-BHC-S4-01-056-005-ZZ-DR-VT-013001	
05		JOH-BHC-S4-01-056-005-ZZ-DR-VT-011001	
06		TQ-OPE-MBL-JCDC-00952 (OPERA ALL LIFT TOP SLAB)	
07		TQ-OPE-MBL-JCDC-00222 (LIFT SHAFT PIT LEVELS)	
08		JCD-OPE-MBL-MR-003-NMR-601-03	
09		JCD-OPE-MBL-MR-003-NMR-602-01	
10		TQ-OPE-MBL-JCDC-00974 (CONFIRMATION OF LIFT DOOR FINISHES)	

REVIEWED BY DISCIPLINE	SIGNATURE	DATE
ARCHITECTURAL	MT	2026-07-19
STRUCTURAL	PC	2026-07-19
MECHANICAL	SH.A	2026-07-19
PLUMBING	SH.A	2026-07-19
ELECTRICAL	SH.A	2026-07-19
ICT	SH.A	2026-07-19
ADDITIONAL DISCIPLINES TO BE ADDED AS REQUIRED		

REV	DATE	BY	DESCRIPTION	CHK	APD
S01	08-JULY-2026	AK	Shop Drawing	SS	AB
S00	08-JULY-2026	AK	Issued for Approval	SS	AB

DRAWING STATUS:
CONSTRUCTION SHOPDRAWING

CLIENT:
شركة وسط جدة للتطوير
Jeddah Central Development Co.

LEAD DESIGN CONSULTANTS:
Henning Larsen

LEAD ENGINEERING CONSULTANT:
BURO HAPPOLD

PROJECT SUPERVISION CONSULTANT:
KHATIB & ALAMI

GENERAL CONTRACTOR:
MBL

REVIEWER:
dar

SUB CONTRACTOR:
OTIS ELEVATOR COMPANY (SAUDI ARABIA) LIMITED
OTIS

PROJECT
JEDDAH OPERA HOUSE

TITLE:
OPERA BUILDING
VERTICAL TRANSPORTATION
PART 001
PLANS - LIFT SHAFT (L05)


SCALE @ A1:	CHECKED:	APPROVED:
As indicated	SS	AB

PROJECT No:	DESIGNED:	DRAWN:	DATE:
440014	AK	PR	08-JULY-2026

DRAWING No: JOH-OTS-S5-01-056-001-ZZ-SD-VT-011010 REV: S01

MODEL FILE REF: JOH-OTS-S5-01-056-XXX-ZZ-M3-VT-010001


ⓒ JCDC

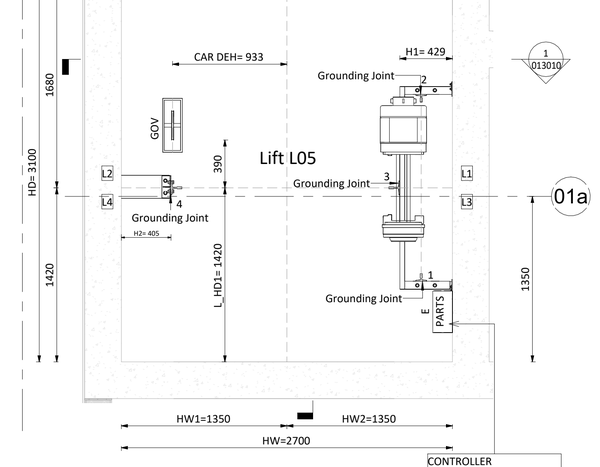

CONTROLLER
-WIFI (By Main Contractor)
-BMS (By Main Contractor)
-EMS (By Main Contractor)
-CCTV (By Main Contractor)
-Fire (By Main Contractor)
-Cabin BGM Speakers
(By Main Contractor)


4 Machine Plan Level - ELEV-L5

1 : 25

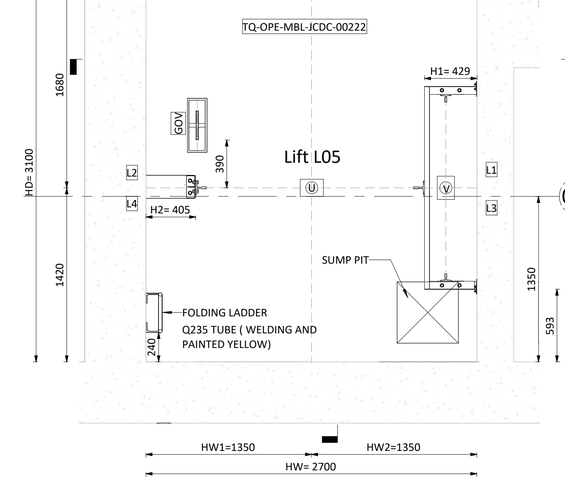


5 Hoist Way Pit Plan - ELEV-L5

1 : 25

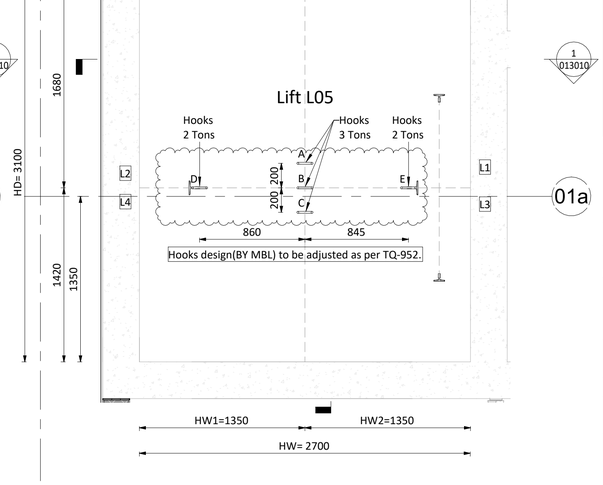

6 Top Hoist Way Hook Plan - ELEV-L5

1 : 25



SCEC – K&A Reviewed
Civil
Arch.
Elec.
ELV.
Mech.
Acoustic

SCEC – K&A Reviewed
Code B – Approved with Comments
(Do not Resubmit)

K&A COMMENTS

COMPLY WITH CRS COMMENTS


Disclaimer :K&A Khatib Alami – Saudi Consolidated Engineering review and/or approval does not relieve the Contractor from obligation to adhere to Contract Documents. The Contractor remains fully responsible for the accuracy, completeness, coordination, and compliance of all submitted documents and works.

the Note provided on the drawing is rejected and the word (by client)shall be replaces to (by main contractor):

Refer to Attached CRS:
SD-OPE-MBL-JCDC-01848-00 k&A comments_1-version-(0_00) (lift 5)

dar Checked and Reviewed


CONTROLLED COPY
MBL IFC
JEDDAH OPERA HOUSE PROJECT
QA/QC Department
MBL QAM
Engr. Mudassar Altaf

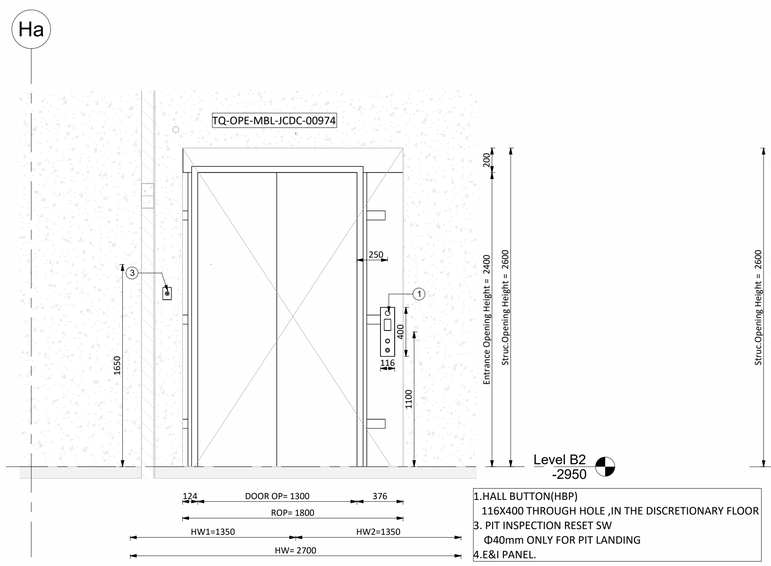

1.HALL BUTTON(HBP)
116X400 THROUGH HOLE ,IN THE DISCRETIONARY FLOOR
3. PIT INSPECTION RESET SW
Φ40mm ONLY FOR PIT LANDING
4.E&I PANEL.


1 Door Elevation At "B2" Floor - ELEV-L5

1 : 25

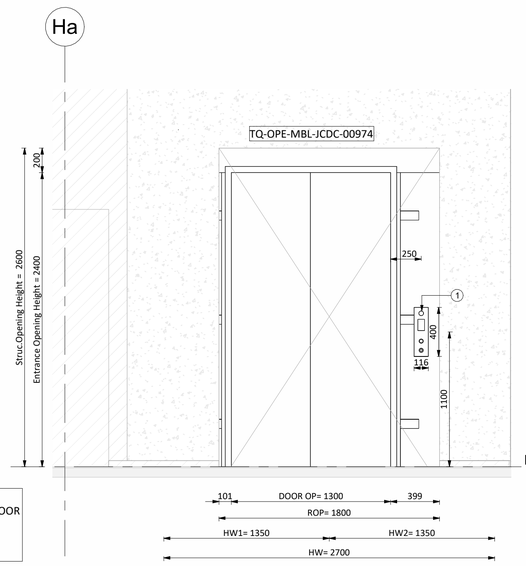


2 Door Elevation At "G" Floor - ELEV-L5


1 : 25

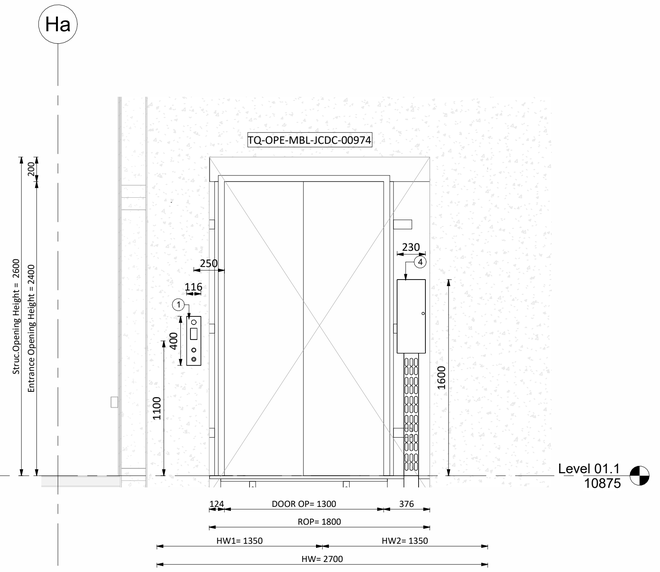

3 Door Elevation At "Top" Floor - ELEV-L5

1 : 25





KEY PLAN


GENERAL NOTES: ALL LEVELS SHOWN ON THE DRAWING ARE CHART DATUM LEVELS PROJECT LEVEL+0.000 = +3.700 CHART DATUM.

K&A Comments :

call button centerline height of 1100 mm is ok subject that the installation remains fully compliant with EN 81-70 and the applicable accessibility requirements


CCOMPLY WITH CRS COMMENTS

Disclaimer :K&A Khatib Alami – Saudi Consolidated Engineering review and/or approval does not relieve the Contractor from obligation to adhere to Contract Documents. The Contractor remains fully responsible for the accuracy, completeness, coordination, and compliance of all submitted documents and works.

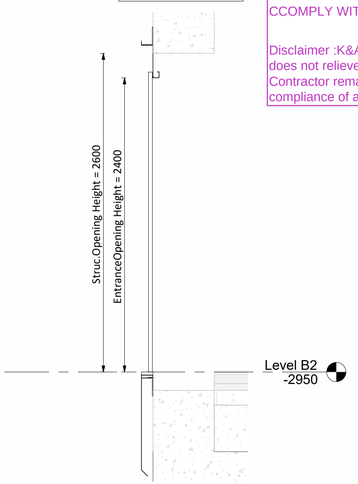


4 Cross-Section View A-A - ELEV-L5

1 : 25




5 E&I SPOT DETAIL - ELEV-L5


1 : 25

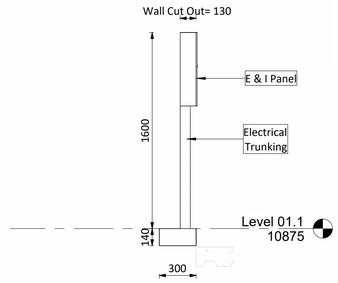

6 Cross-Section View B-B - ELEV-L5

1 : 25





Protection Elevation Detail
At Each Elevator Shaft Opening

LEGEND	
HW	HOIST WAY WIDTH
HD	HOIST WAY DEPTH
CRH	CAR ROUGH HEIGHT
DOOR OP	DOOR OPENING
ROP	ROUGH OPENING
CW	CAR WIDTH
CD	CAR DEPTH
CH	CAR HEIGHT
DBG	DISTANCE BETWEEN GUARDRAIL
CWT	COUNTERWEIGHT
E&I PANEL	EMERGENCY & INSPECTION PANEL
G.O.V	CAR GOVERNOR
COP	CAR OPERATING PANEL
HBP	HALL BUTTON POSITION INDICATOR

SCEC – K&A Reviewed
Civil
Arch.
Elec.
ELV.
Mech.
Acoustic

SCEC – K&A Reviewed
Code B – Approved with Comments
(Do not Resubmit)

Refer to Attched CRS:
SD-OPE-MBL-JCDC-01848-00 k&a comments_1-version-(0_00) (lift 5)

dar Checked and Reviewed

CONTROLLED COPY MBL IFC JEDDAH OPERA HOUSE PROJECT QA/QC Department
MBL QAM
Engr. Mudassar Altaf

DRAWING / DOCUMENT REFERENCE

NO.	NUMBER	TITLE	REV.
01	L-05	JOH-HLA-S4-01-056-XXX-01-DR-AR-011110	F00
02		JOH-BHC-S4-01-056-XXX-XX-DR-VT-015001	
03		JOH-BHC-S4-01-056-XXX-XX-DR-VT-010001	
04		JOH-BHC-S4-01-056-005-ZZ-DR-VT-013001	
05		JOH-BHC-S4-01-056-005-ZZ-DR-VT-011001	
06		TQ-OPE-MBL-JCDC-00952 (OPERA ALL LIFT TOP SLAB)	
07		TQ-OPE-MBL-JCDC-00222 (LIFT SHAFT PIT LEVELS)	
08		JCD-OPE-MBL-MR-003-NMR-601-03	
09		JCD-OPE-MBL-MR-003-NMR-602-01	
10		TQ-OPE-MBL-JCDC-00974 (CONFIRMATION OF LIFT DOOR FINISHES)	

REVIEWED BY DISCIPLINE	SIGNATURE	DATE
ARCHITECTURAL	MT	2026-07-19
STRUCTURAL	PC	2026-07-19
MECHANICAL	SA A	2026-07-19
PLUMBING	SA A	2026-07-19
ELECTRICAL	SA A	2026-07-19
ICT	SA A	2026-07-19
ADDITIONAL DISCIPLINES TO BE ADDED AS REQUIRED		

REV	DATE	BY	DESCRIPTION	CHK	APD
S01	08-JULY-2026	AK	Shop Drawing	SS	AB

DRAWING STATUS: CONSTRUCTION SHOPDRAWING

CLIENT: شركة وسط جدة للتطوير Jeddah Central Development Co.

LEAD DESIGN CONSULTANTS: Henning Larsen

LEAD ENGINEERING CONSULTANT: BURO HAPPOLD

PROJECT SUPERVISION CONSULTANT: KHATIB & ALAMI

GENERAL CONTRACTOR: MBL

REVIEWER: dar

SUB CONTRACTOR: OTIS ELEVATOR COMPANY SAUDI ARABIA LIMITED — OTIS

PROJECT: JEDDAH OPERA HOUSE


TITLE: OPERA BUILDING
VERTICAL TRANSPORTATION
PART 001
ELEVATIONS - LIFT SHAFT (L05)

SCALE @ A1:	CHECKED:	APPROVED:	
As indicated	SS	AB	
PROJECT No:	DESIGNED:	DRAWN:	DATE:
440014	AK	PR	08-JULY-2026

DRAWING No: JOH-OTS-S5-01-056-001-ZZ-SD-VT-012010 REV: S01


MODEL FILE REF: JOH-OTS-S5-01-056-XXX-ZZ-M3-VT-010001

© JCDC

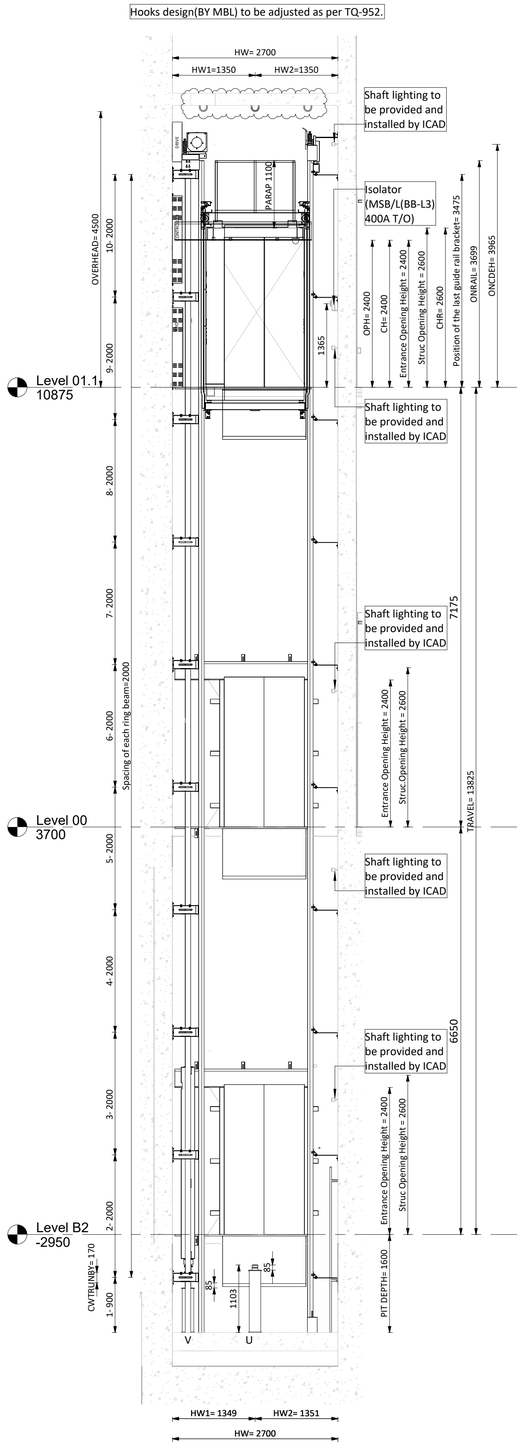


1 Section "A" - ELEV-L5

1 : 50

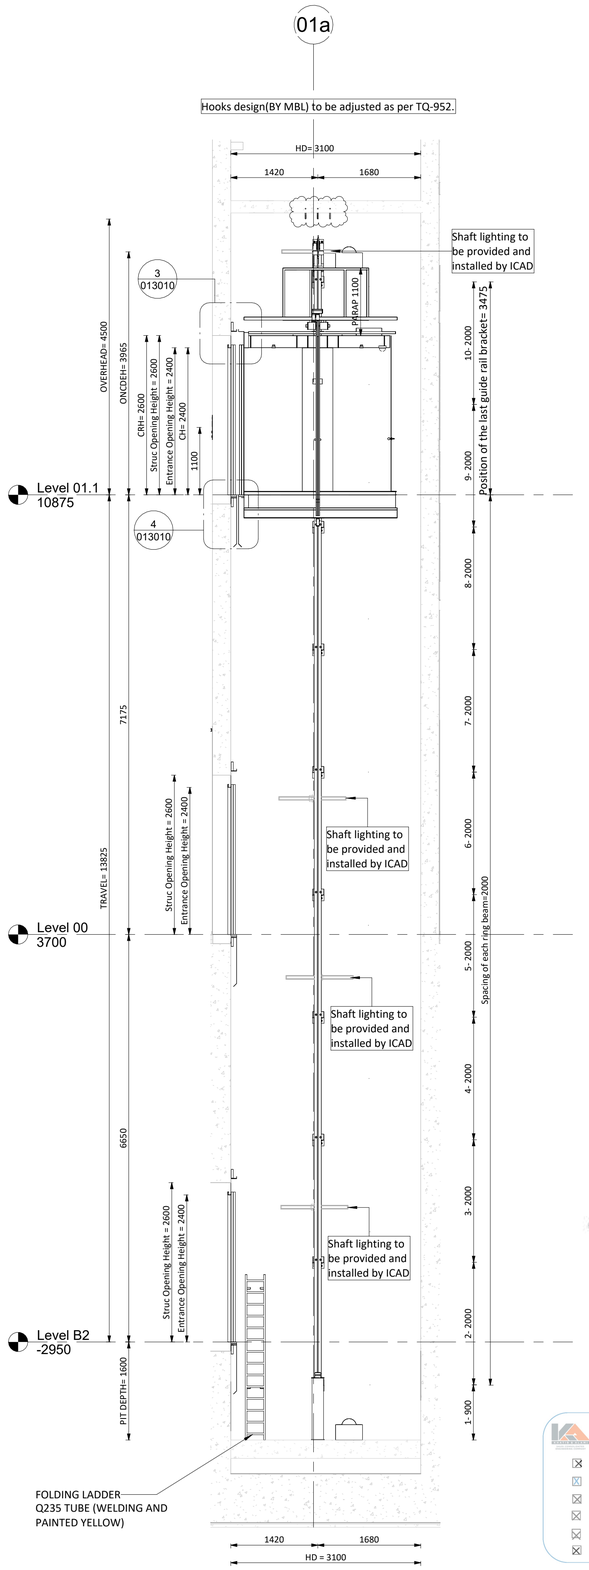


2 Section "B" - ELEV-L5

1 : 50

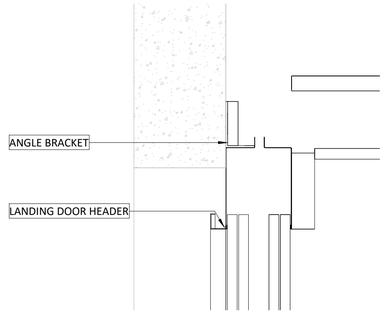

3 Landing Door Header Detail - ELEV-L5

1 : 10

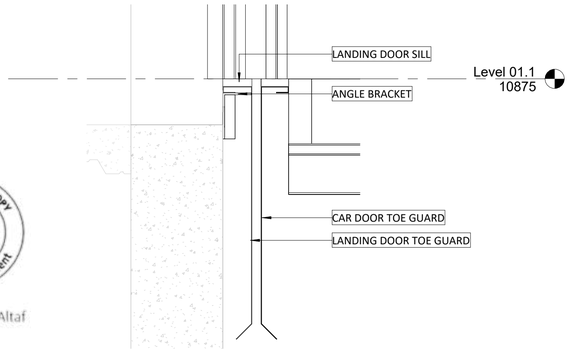

4 Landing Door Bottom Detail - ELEV-L5

1 : 10

CONTROLLED COPY
MBL IFC
JEDDAH OPERA HOUSE PROJECT
QA/QC Department
MBL QAM
Engr. Mudassar Altaf

SCEC – K&A Reviewed
Civil
Arch.
Elec.
ELV.
Mech.
Acoustic

SCEC – K&A Reviewed
KHATIB & ALAMI
SAUDI CONSOLIDATED ENGINEERING COMPANY
Code B – Approved with Comments (Do not Resubmit)


K&A COMMENTS


COMPLY WITH CRS COMMENTS

Disclaimer :K&A Khatib Alami – Saudi Consolidated Engineering review and/or approval does not relieve the Contractor from obligation to adhere to Contract Documents. The Contractor remains fully responsible for the accuracy, completeness, coordination, and compliance of all submitted documents and works.

dar
Checked and Reviewed

Refer to Attached CRS:
SD-OPE-MBL-JCDC-01848-00 k&A comments_1-version-(0_00) (lift 5)





KEY PLAN

GENERAL NOTES: ALL LEVELS SHOWN ON THE DRAWING ARE CHART DATUM LEVELS PROJECT LEVEL+0.000 = +3.700 CHART DATUM.

DRAWING / DOCUMENT REFERENCE

NO.	NUMBER	TITLE	REV.
01	L-05	JOH-HLA-S4-01-056-XXX-01-DR-AR-011110	F00
02		JOH-BHC-S4-01-056-XXX-XX-DR-VT-015001	
03		JOH-BHC-S4-01-056-XXX-XX-DR-VT-010001	
04		JOH-BHC-S4-01-056-005-ZZ-DR-VT-013001	
05		JOH-BHC-S4-01-056-005-ZZ-DR-VT-011001	
06		TQ-OPE-MBL-JCDC-00952 (OPERA ALL LIFT TOP SLAB)	
07		TQ-OPE-MBL-JCDC-00222 (LIFT SHAFT PIT LEVELS)	
08		JCD-OPE-MBL-MR-003-NMR-601-03	
09		JCD-OPE-MBL-MR-003-NMR-602-01	
10		TQ-OPE-MBL-JCDC-00974 (CONFIRMATION OF LIFT DOOR FINISHES)	

REVIEWED BY DISCIPLINE	SIGNATURE	DATE
ARCHITECTURAL	MT	2026-07-19
STRUCTURAL	PC	2026-07-19
MECHANICAL	SH.A	2026-07-19
PLUMBING	SH.A	2026-07-19
ELECTRICAL	SH.A	2026-07-19
ICT	SH.A	2026-07-19
ADDITIONAL DISCIPLINES TO BE ADDED AS REQUIRED		

REV	DATE	BY	DESCRIPTION	CHK	APD
S01	08-JULY-2026	AK	Shop Drawing	SS	AB
S00	08-JULY-2026	AK	Issued for Approval	SS	AB

DRAWING STATUS: CONSTRUCTION SHOPDRAWING

CLIENT: Jeddah Central Development Co.

LEAD DESIGN CONSULTANTS: Henning Larsen

LEAD ENGINEERING CONSULTANT: BURO HAPPOLD

PROJECT SUPERVISION CONSULTANT: KHATIB & ALAMI

GENERAL CONTRACTOR: MBL

REVIEWER: dar

SUB CONTRACTOR: OTIS ELEVATOR COMPANY (SAUDI ARABIA) LIMITED — OTIS

PROJECT: JEDDAH OPERA HOUSE

TITLE: OPERA BUILDING
VERTICAL TRANSPORTATION
PART 001
SECTIONS - LIFT SHAFT (L05)

SCALE @ A1:	CHECKED:	APPROVED:
As indicated	SS	AB

PROJECT No:	DESIGNED:	DRAWN:	DATE:
440014	AK	PR	08-JULY-2026

DRAWING No: JOH-OTS-S5-01-056-001-ZZ-SD-VT-013010 REV: S01

MODEL FILE REF: JOH-OTS-S5-01-056-XXX-ZZ-M3-VT-010001

© JCDC
